

Work Order ID 132517

May-07-15 2:50:02 PM

132517

Page 1

Item ID: D3281-1L08 Accept ***N900040100*** Setup Start ***NS1***
 Revision ID: Stop ***NS2***
 Item Name: Floor Protector, Fwd LH
 Start Date: 5/05/15 Start Qty: 2.00 ***2*** Cust Item ID:
 Required Date: 5/07/15 Req'd Qty: 2.00 ***2*** Customer:
 Reference:

Approvals: Process Plan: W Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D3281	Rev F

100		0.00							
100	HAND FINISHING THERMOFORMING					2			
Thermoform	Memo	0.00							
Thermoforming Machine	Cut Blanks								

105		0.00							
105	Dry Material					x2			DAS 07 9-89
HandThermo	Memo	0.00							
Hand Finishing Thermoforming	Dry Sheet as per QSI022 POLYCARBONATE								

Temp: 245 deg. F
 Time IN: 5:00 PM
 Time OUT: 6:00 AM
 MAY 13 2015
 Per: _____

15/05/13

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabelled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : ☐					

Work Order ID 132517

132517

Page 2

May-07-15 2:50:02 PM

Item ID: D3281-1L08 Accept *N900040100* Setup Start *NS1*
 Revision ID: Stop *NS2*
 Item Name: Floor Protector, Fwd LH
 Start Date: 5/05/15 Start Qty: 2.00 *2* Cust Item ID:
 Required Date: 5/07/15 Req'd Qty: 2.00 *2* Customer:
 Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start *NR1*
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
110 *110* Thermoform Thermoforming Machine	THERMOFORMING MACHINE Memo Thermoform as per Dwg. D3281 and Folio FTA 011 Dwg. Rev. <u>DF</u> Folio Rev. <u>D</u>	0.00 0.01				<u>2</u>			<u>3/5/ps/13</u> <u>P10</u> →
130 *130* Thermoform Thermoforming Machine	HAND FINISHING THERMOFORMING Memo Trim to Finished Dimensions	0.00 0.01				<u>x2</u>			<u>DAS</u> <u>07</u> <u>9-89</u> <u>15/05/19</u>
140 *140* QC Quality Control	QC2- Inspect parts off machine FAI/FAIB Memo	0.00 0.00				<u>x2</u>			<u>DAS</u> <u>07</u> <u>9-89</u> <u>15/05/19</u>

DQA:

Date: 16.03.10



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed:

Date: 16/04/18

Work Order update only ☐

Work Order: <u>132517</u> Part No. <u>D3281-1L08</u> NCR No. <u>15-5730</u>		DISPOSITION Rework ☐ Scrap ☒ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Cross tube ☐ Water Jet ☐ Engineering ☐ Machining ☐ Small Fab ☐ Prod. Eng. Coord. ☐ Quality ☐ Thermoforming ☒ Finishing ☐ Rec/Store/Packaging ☐ Other ☐ Large Fab ☐ Composite ☐ Supplier ☐			
Date: <u>15/05/19</u>		Step #: <u>110</u>		QTY Effective: <u>1</u>		MRB (QS1042) Approval	
Description Work Order Deviation				Disposition		<u>8/15/19</u> Completed By <u>For BB 15/05/19</u> Lead hand / Supervisor Approval Verification <u>Wh. 15/05/19.</u> QC / QA Coordinator Approval <u>AD 15-05-28</u>	
Dirt in mould. R.C. operator not verifying his mould before working on it				Scrap & Replace 1 part.			
Root Cause Environment ☐ No Re-verification ☐ Design ☐ Operator ☒ Doc/Data ☐ Offset/Setup ☐ Equip/Tooling ☐ Supplier ☐ Handling/Pre ☐ Training ☐ Material ☐ Use for Testing ☐ Internal Transport ☐ Poor Information ☐ Tribal Knowledge ☐ Rushing ☐ LOA ☐ Product Improvement ☐ Substation ☐ Process Improvement ☐ Past Expiry Date ☐ Manufacturing Process ☐ Misidentified ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Temperature/Cure ☐ Power Loss/Surge ☐ Positioned Wrong ☐ Bending ☐ Set-up ☐ Folio/Program ☐ Outside Dimensions ☐ Centre Not Concentric ☐ BOM/Route ☐ Grain ☐ Over/Under tolerance ☐ Cracks ☐ Broken/Damage/Defect ☒ Weld ☐ Part Incorrect ☐ Crimp/Kink/Ripple/Wave ☐ Inspection Incomplete/Unqualified ☐ Wrong Stock Pulled ☐ Part Lost/Missing ☐ Cuffs ☐ Contamination ☐ Out of Sequence ☐ Part Moved ☐ Crushing ☐ Countersink ☐ Off-set ☐ Drawing ☐ Heat Treat ☐ Cut Too Short ☐ Misabeled ☐ Finish ☐ Wave/Twist in Tube ☐ Instructions Incomplete/Unclear ☐ Fit/Function ☐ Misread ☐ Marks/Chatter ☐ Drill Holes ☐ Misaligned/off center ☐ Turning Sequence ☐					
OTHER: ☐							

Work Order ID 132517

132517

Page 3

May-07-15 2:50:02 PM

Item ID: D3281-1L08 Accept *N900040100* Setup Start *NS1*
 Revision ID: Stop *NS2*
 Item Name: Floor Protector, Fwd LH
 Start Date: 5/05/15 Start Qty: 2.00 *2* Cust Item ID:
 Required Date: 5/07/15 Req'd Qty: 2.00 *2* Customer:
 Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start *NR1*
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
150	QC5- Inspect part completeness to step on W/O	0.00							DAS 38 9-89
150						(2)			MAY 25 2015
QC	Memo	0.00							
Quality Control									
160	Packaging	0.00							MAY 25 2015
160									28 9-89
Packaging	Memo	0.00							
Packaging									
170	QC21- Final Inspection - Work Order Release	0.00							MAY 26 2015
170									MLJ
QC	Memo	0.00							
Quality Control									

MLJ

MAY 26 2015

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QS1042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabelled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : ☐					

Picklist Print

May-07-15 2:50:02 PM

Page 1

Work Order ID: 132517

132517

Parent Item: D3281-1L08

D3281-11 08

Parent Item Name: Floor Protector, Fwd LH

Start Date: 5/05/15

Required Date: 5/07/15

Start Qty: 2.00

Required Qty: 2.00

Comments: IPP Rev. A 10.02.24 New Issue LL
Add Step 105 Dry Material 10/04/21 DL

IPP Rev. B

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
MLEXS.118-90318-08		Purchased	No			100	sf	1,571.000	5	11			DAS 07 9-09
MI FXS 118-90318-08										**			

Lexan Sheet

Location

therm

m126994

Loc Qty

1571

1571

Loc Code

16.5 sg ft.

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QS1042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabelled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : ☐					

DART AEROSPACE LTD		Work Order: 132517
Description: Floor Protector, Fwd LH		Part Number: D3281-1
Inspection Dwg: D3281	Rev: F	Page 1 of 1

FIRST ARTICLE INSPECTION CHECKLIST
THERMOFORMING SECTION

Description	Accept	Reject	Method of Inspection	Comments
Inside Radii less than 0.1875" Go/No Go	✓			
Shape Definition	✓			
Texture Retention	✓			
Material imperfections such as bumps, cracks, voids, scratching	✓			

Measured by: *JB*

Date: 15/05/19

TRIMMING SECTION

Drawing Dimension	Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
18.6	+/-0.100	18.6"	✓			
17.1	+/-0.100	17.1"	✓			
11.7	+/-0.100	11.7"	✓			
0.95	+/-0.030	0.98"	✓			
0.25	+/-0.030	0.27"	✓			
0.030	Min	0.068"	✓			
0.070	Min	0.090"	✓			

DAS

Measured by: 07
9-88

Date: 15/05/19

Audited by: *JB*



Date: 15/05/28

Preliminary Approval:

Date:

Rev	Date	Change	Revised by	Approved
A	08.02.28	New Issue	KJ/DL	
B	08.04.16	Dimensions updated per Dwg Rev D	KJ/DL	
C	08.09.12	Tolerance revised for 0.070 dimension	KJ/DL	
D	10.09.01	Dwg Rev updated	KJ	
E	11.06.21	Dwg Rev updated	KJ	

132517

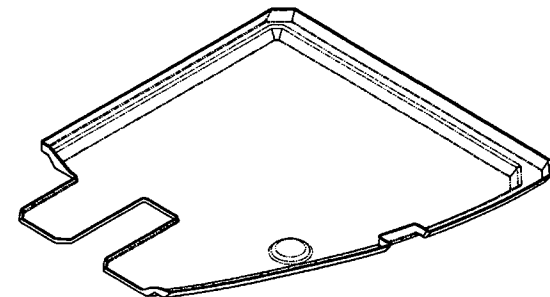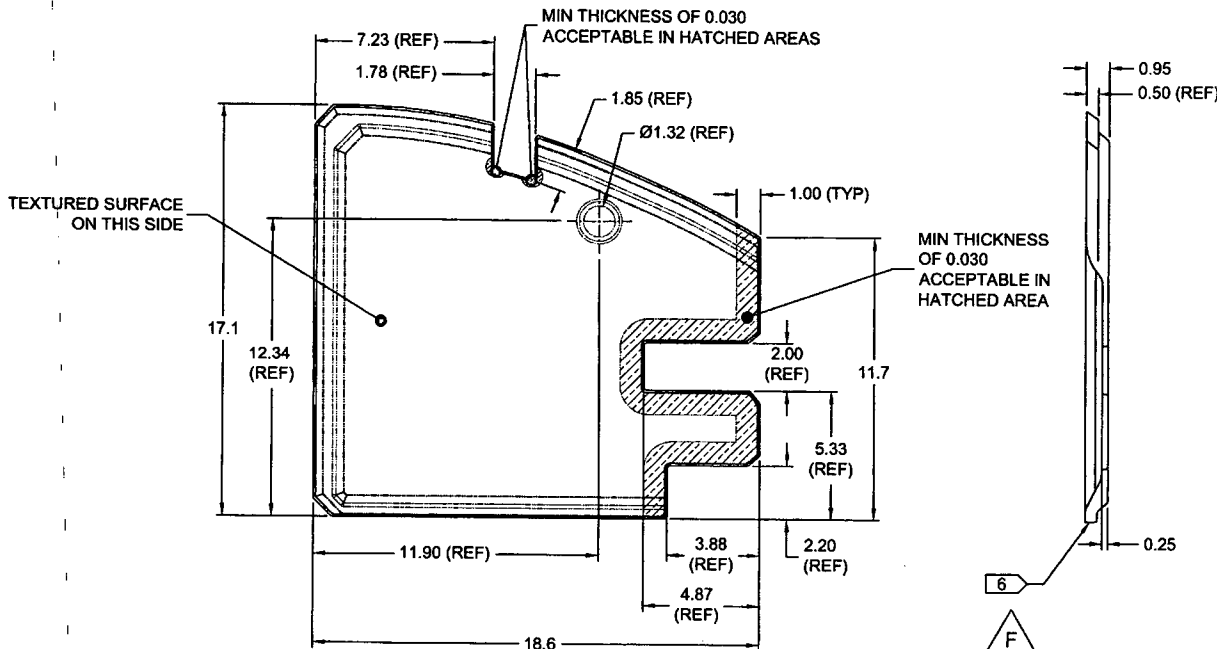


RELEASED
2010-11-25

D3281-1 FLOOR PROTECTOR

NOTES:

- 1) MATERIAL: -1L02 = LEXAN F6006, BLACK No. 701, 0.093" THICK (MLEXS.093-F6006-02)
-1L08 = LEXAN 90318 (PROTECT-A-GLAZE), 0.118 THICK, 112-CLEAR (MLEXS.118-90318-08)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.010 MAX
- 6) IDENTIFICATION: IDENT WITH DART P/N "D3281-1Lxx" AND B/N PER QSI 044 6.4 ALONG PERIMETER OF PART AS SHOWN.
- 7) WEIGHT: D3281-1L02 = 0.95 lb D3281-1L08 = 1.13 lb
- 8) THERMOFORM WITH MOLD D3281-1T1 PER DART QSI 022; TRIM AS SHOWN
MINIMUM THICKNESS AFTER FORMING: 0.070" EXCEPT WHERE INDICATED

F	NOTES UPDATED. FLAG NOTE 6 WAS 7 & RELOC, D.E.O. D3281-E-1 INC. DIM 17.0 WAS 17.1 (ZN B5-3, B6-4) & 17.7 WAS 17.8 (ZN C5-3, C6-4) REF CAR 10-21.	JPH	10.09.27
E	-3/4 NOW TRIMMED FLAT: RMV 0.25 BEVEL TO FACILITATE TRIMMING (ZN D6-3, D4-4)	CP	10.01.05
D	THICKNESS 0.093 WAS 0.125, MIN THICKNESS 0.070 WAS 0.080, P/N AND B/N ID WITH VIBRATING STYLUS (ZN A7-1, A7-2, A7-3, A7-4); D3281-4 NOW ON PAGE 4; CORRECT WEIGHTS (ZN A8-1, A8-2, A8-3, A8-4)	PH	08.03.28
C	UPDATE DIMS TO MATCH PARTS: COLOUR 701 WAS 700; GENERAL UPDATE	LE	07.10.09
B	NOW LEXAN; DIMS AS MANUFACTURED	CP	05.11.25
A	NEW ISSUE	CP	04.05.03
REV.	DESCRIPTION	BY	DATE
DESIGN	 DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA DRAWING NO. D3281 TITLE FLOOR PROTECTOR SCALE NTS COPYRIGHT © 2004 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR REPRODUCED OR TRANSMITTED IN ANY FORM OR BY ANY MEANS WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	REV. I OF 1	
DRAWN			
CHECKED			
MFG. APPR.			
APPROVED			
DE APPR.			
DATE	10.09.27		
